WBS	IRTPO CPT-HSTP UPDATE TIMELINE	Start	Finish
1	Kick-off meeting with IRTPO Planner and representatives	5/2/22	5/2/22
3	Data collection and analysis	5/2/22	7/8/22
3	Creation of preliminary draft outline	5/3/22	5/13/22
2	Coordination with IRTPO Transportation Planner (TP)	5/16/22	5/20/22
1	Technical Equity Committee (TEC) meeting	5/18/22	5/18/22
5	DRAFT Plan #1 for review by IRTPO TP and TEC	5/23/22	6/10/22
1	TEC meeting to discuss draft plan, project and needs analysis	6/13/22	6/13/22
5	DRAFT Plan #1 to IRTPO TP for Executive Board (EB) packets/posting	6/15/22	6/15/22
1	EB meeting to review/discuss preliminary draft and project list	6/22/22	6/22/22
4	IRTPO TP to advertise public meeting	6/22/22	6/22/22
5	Revision of Draft Plan #1 based on EB comments	6/22/22	6/29/22
4	DRAFT Plan #2 to IRTPO TP for posting to website	7/1/22	7/1/22
4	Virtual public meeting on HSTP	7/6/22	7/8/22
1	Final TEC meeting to prioritize projects	~~7/11/22~~	~~7/11/22~~
5	Revisions to DRAFT Plan #2 and project list based on TEC comments	~~7/18/22~~	~~8/12/22~~
4	IRTPO TP to advertise public review and comment period	8/10/22	8/10/22
4	DRAFT Plan #3 to IRTPO TP to post on IRTPO/partner agency websites	~~8/12/22~~	~~8/12/22~~
4	Public review and comment period	8/23/22	10/21/22
5	**Formal DRAFT CPT-HSTP due to WSDOT**	8/31/22	8/31/22
1/4	EB Meeting #2 and Public Meeting #2	9/28/22	9/28/22
4	Public hearing on DRAFT Plan and prioritized project list	9/28/22	9/28/22
6	Compilation of all comments	10/24/22	10/28/22
6	Revision of document based on comments	10/24/22	11/14/22
6	FINAL Plan, Comment/Response Log to IRTPO TP for EB packets/posting	11/15/22	11/15/22
6	IRTPO EB action on FINAL CPT-HSTP	11/23/22	11/23/22
6	**Submittal of adopted FINAL CPT-HSTP to WSDOT**	12/1/22	12/1/22

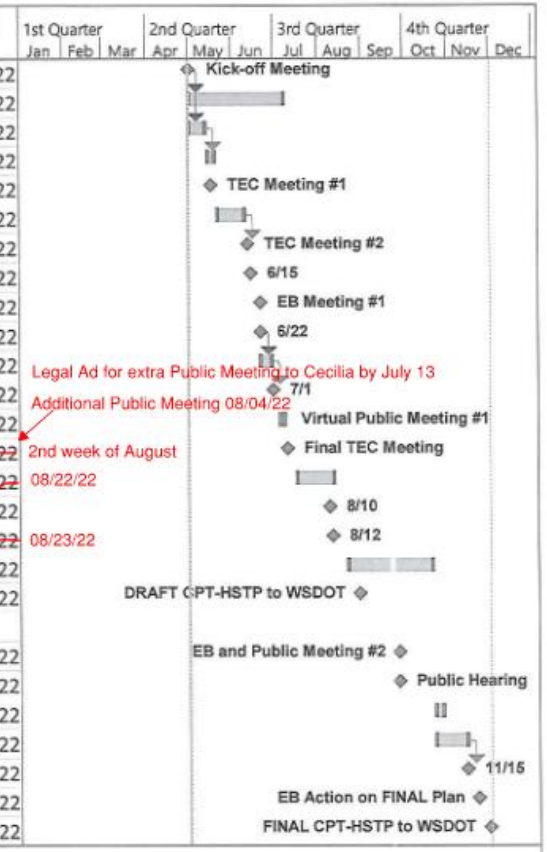

CPT-HSTP
Date: 4/5/22

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
